





Interplanetary Network Directorate (IND)
Deep Space Network (DSN)
Resource Allocation Planning Service




Jet Propulsion Laboratory
California Institute of Technology

DSN Antenna Downtime Status and Forecast





Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




Antenna Downtime Status and Forecast

Downtime	Antenna	Start Date	End Date	Weeks	POC	Notes
Complex downtime for NMC Automated Link Build (ALB) and Acceptance testing	GDSCC	Mar 2013 Jan 2014	Oct 2013 Jan 2014	10, 12, 17, 24, 32, 38, 43, 49, 03	Jim Buckley, Dave Taylor, Shirley Cizmar	Request 6 – 8 hours each block – days/times flexible. Moved week 42 NMC ALB task to week 43 due to LADEE contention and viewperiod. An additional request for NMC ALB A/T was added in week 49. Week 49 remains to be completed. Added week 03 of 2014 for A/T
HEF Maser Replacement	DSS-15	Sep 9 2013	Dec 21 2013	37 – 51	Anna Fan, Chris Link	Replacing Maser LNA with HEMT LNA, 250W S-Band, Depot Level Maintenance, Gain Select Installation all NIB. Demo tracks planned for week 48 because of project activities for Comet ISON Observing Campaign. DSS-15 returned to service DOY 345/0200. Planned 11 hours maintenance blocks are scheduled DOYs 345, 346, 347, 350, 351 & 352 1500-0200. The remaining time is available for tracking.
HBI Calibrations	DSS-63	Nov 2013	Nov 2013	45/46	Bernardo Lopez, Asim Sehic	Request 2 night time 10 – 12 hour blocks for calibration of the current “10 degree bar” and “3.33 degree bar”. This work is very critical in establishing where in the 360 degrees of azimuth travel before we start the epoxy regROUT in March. Moved to Nov 2013 time frame Completed



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




Antenna Downtime Status and Forecast

Downtime	Antenna	Start Date	End Date	Weeks	POC	Notes
Complex downtime for NMC Automated Link Build (ALB) and SOAK	GDSCC	Jan 2014	Jan 2014	05	Jim Buckley, Shirley Cizmar, Dave Taylor	Request 6 – 8 hours per block at each complex A management decision was made to move DSOC and GDSCC from week 08 to week 05. DSOC is scheduled to be completed prior to NMC ALB and is not network wide downtime – JPL only
	DSOC	Feb 2014	Feb 2014	07		
	MDSCC	Mar 2014	Mar 2014	10		
Complex downtime for Power House Commission	CDSCC	March 2014	Oct 2014	12, 14, 18, 30, 51	John Phillips, Rob Mehrkish, Dave Taylor	Downtimes shifted to new dates. Prime shift hours are preferred. Week 12 downtime requires 12 hours. Downtimes in weeks 14, 18, 30, and two in week 51 require 6 hours Week 33 downtime requires 12 hours, week 35 downtime requires 6 hours.
		March 2015	March 2015	33, 35		
HBA Prep Metrology – AZ Runner Measurement	DSS-63	Feb 4 2014	Feb 7 2014	06	Tim Sink	Requested 4 additional nights 12 hours each Jan/Feb 2014 timeframe – The first night of downtime was reduced to 6 hours 20 minutes to accommodate Cassini's T98 P/B pass
Grouting	DSS-63	2014	2014	09 – 15	Pam Rothman, Dave Taylor, David Munoz, Mochon, Bernardo Lopez, Asim Sehic	An additional week was added to first grouting in 2014 in preparation for the DSN 50th anniversary. Nov 2014, S-Band Maser Replacement NIB May 2015, 70m Tune-up and calibration NIB 2015 groutings are only 2 weeks to allow support of NHPC Have the option of two 5 weeks downtimes in 2017, could removed HBA Upgrade or take a single 10 weeks downtime in 2017. Need at least 8 weeks in 2017 if the APCA is NIB to downtime
		2014	2014	44 – 48		
		2015	2015	19 & 20		
		2015	2015	32 & 33		
		2016	2016	14 – 17		
		2016	2016	40 – 43		



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




Antenna Downtime Status and Forecast

Downtime	Antenna	Start Date	End Date	Weeks	POC	Notes
Complex downtime for SPC-60 Power Cutover	MDSCC	Apr 2014	Aug 2014	15, 19, 23, 27, 31, 34	Anna Fan, Rob Mehrkish, Javier Lopez-Perea	Request 12 hours blocks of prime shift hours, but hours are negotiable. Weeks 7 & 11 were moved to weeks 31 & 34. Week 34 is the last downtime for this task. They may have to compress time between specific dates and hours for each downtime.
DSOC & DCD 4.1 software installation	GDSCC DSOC	Feb 2014	Feb 2014	09	Anna Fan, Sheila Garrett	A management decision was made to move DSOC and DCD to week 09 to run with the Network wide GNM task
	CDSCC	Apr 2014	Apr 2014	14		Data at CDSCC and MDSCC will be spooled at the complex and delivered after the downtime is complete. CDSCC/MDSCC will be scheduled after GDSCC S/W installation
	MDSCC	Apr 2014	Apr 2014	17		Moved from week 16 to week 17 due to Easter Holiday
Modkit Install	DSS-35	Jan 2014	Mar 2014	01 – 11	John Phillips for CDSCC	DSS-35 Modkit installation during Jan – Mar time frame
HBA Shimming	DSS-43	April 2014	May 2014	16 – 18	David Munoz for MDSCC	DSS-43 changed to HBA Shimming and 2400 Vac Alternate Bus Installation will be NIB
Depot Level Maintenance	DSS-45	May 2014	May 2014	19 – 21	David Munoz for MDSCC	DSS-45 DLM was moved to accommodate mission supports
	DSS-65	May 2014	June 2014	22 – 24		DSS-65 DLM was moved to accommodate mission supports
	DSS-34	Jan 2015	Feb 2015	05 – 08		



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




Antenna Downtime Status and Forecast

Downtime	Antenna	Start Date	End Date	Weeks	POC	Notes
Antenna Inspections	MDSCC	April 2014 Aug 2017	April 2014 Aug 2017	14 & 15 35 & 36	Dave Taylor, Neil Bucknam	MDSCC Inspections times moved from weeks 12 & 13 to weeks 14 & 15
Electrical Maintenance	DSS-24,25,26	April 2014	May 2014	16 & 19	David Lloyd, Erik Holmgren	Requesting downtime for preventative maintenance blocks to update electrical items
Complex wide Electrical Maint.	SPC-10	May 2014	May 2014	22		This 12-hour downtime will end at 0100, one hour before Cassini's activities
Elevation Cable Wrap	DSS-15	June 2014	July 2014	25 – 27	Marwah Buck	Moved from weeks 29-31. Swap with 80kW Prep.
Replace Sub Reflector Cable	DSS-14	Jul 2014	Jul 2014	28	Erik Holmgren	Request 5 days to perform Sub Reflector Cable replacement Tracking available during night hours after the first 2 nights. Moved from week 07 to week 09 due to GSSR activities.
80kW Prep	DSS-26	July 2014	July 2014	28 - 31	Erik Holmgren	Moved from weeks 23-26. Swap with Elevation Cable Wrap.
Ka U/L Install	DSS-25	Nov 2014	Nov 2014	46	Andre Jongeling	This downtime was requested after the August downtime meeting



Interplanetary Network Directorate (IND)
 Deep Space Network (DSN)
 Resource Allocation Planning Service




Antenna Downtime Status and Forecast

Downtime	Antenna	Start Date	End Date	Weeks	POC	Notes
70M Tune-up and calibration	DSS-14	Dec 1, 2014	Dec 15, 2014	49 & 50	David Allen	These are proposed dates at this time and are In preparation for NHPC Pluto Encounter
	DSS-43	Mar 9, 2015	Mar 21, 2015	11 & 12	John Phillips	
80Kw Facility Prep Task	DSS-26	Jan 2015	June 2015	01 - 26	Pam Rothman, Asim Sehic	After the November downtime meeting, this downtime was moved from weeks 34 - 04, 2015/2016 to weeks 01 - 26 of 2015. AZ Track will be NIB to the 80Kw facility prep task
Antenna Inspections	GDSCC	Mar 2015	Apr 2015	13 & 14	Anna Fan, Neil Bucknam, Daniel Olson	2015 Antenna Inspections moved to March - April timeframe
		Apr 2018	Apr 2018	15 & 16		
AZ Track Replacement	DSS-55	Aug 2015	Oct 2015	34 - 44	Pam Rothman, Asim Sehic	This was moved from weeks 11-21 with the addition of DSS-26 80kW downtime added in weeks 1-26
Antenna Inspections	CDSCC	Jan 2016	Jan 2016	1 & 2	Anna Fan, Dave Taylor, Neil Bucknam, Daniel Olson	2016 - During DSS-45 Maser Replacement



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




Antenna Downtime Status and Forecast

Downtime	Antenna	Start Date	End Date	Weeks	POC	Notes
APCA	DSS-14	Nov 2016	Jan 2017	44 – 04	Anna Fan, Barzia Tehrani	These downtime were requested at July downtime meeting DSS-63 APCA is NIB to HBA and could move based on DSS-63 HBA downtime changes. DSS-14 needs to be scheduled first, DSS-63 and DSS-43 to follow , no preferred order
	DSS-63	Feb 2017	Sept 2017	05 – 36		
	DSS-43	Sept 2017	Nov 2017	37 –		
SWUPS Installation	CDSCC	Nov 2016	Nov 2016	44	Pete Hames	These blocks are proposed at this time 12 hour blocks for each downtime Must be done in daylight. There is a connection to the power house. Would like to move 9 months earlier if possible Will know more in Jan 2014 about moving to beginning of 2016.
		Nov 2016	Nov 2016	46		
		Nov 2016	Nov 2016	48		
HBA Upgrade and Life Extension	DSS-63	Jan 30, 2017	Sep 8, 2017	05 - 36	Dave Taylor, Bernardo Lopez	This is proposed at this time APCA and Maser Replacement are NIB Tentative date, may move to 2018 This is pending a decision of the extension of the grouting blocks to 5 weeks. APCA could be scheduled standalone, but will require at least 12 weeks.
Pedestal Rehab	DSS-54	Jan 8, 2018	Sep 28, 2018	02 - 39	Ben Saldua	This is proposed at this time This date may change based on need Ka2 Tune-up is NIB weeks 36 & 37 and scheduled prior to JWST launch in 2018



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




Jet Propulsion Laboratory
California Institute of Technology

Downtime	Antenna	Start Date	End Date	Weeks	POC	Notes
XX/Ka Installation	DSS-25	Jan 2018	April 2018	01 - 14	Wendy Hodgkin	XX/Ka requires 14 weeks - AZ Track will be NIB in weeks 05-14
	DSS-24	Apr 30, 2018	Jul 9, 2018	18 - 27		Ka2 Tune-up is NIB weeks 18 & 19 and scheduled prior to JWST launch in 2018
Ka2 Tune-up	DSS-34	May 28, 2018	Jun 4, 2018	22 & 23	Wendy Hodgkin	All Ka2 Tune-ups (DSS-24, 34 and 54) must be scheduled prior to JWST launch in October 2018, If JWST launch slips, tune-ups may be slipped also. This is budget/resource driven




Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



Jet Propulsion Laboratory
California Institute of Technology


- 2013 -

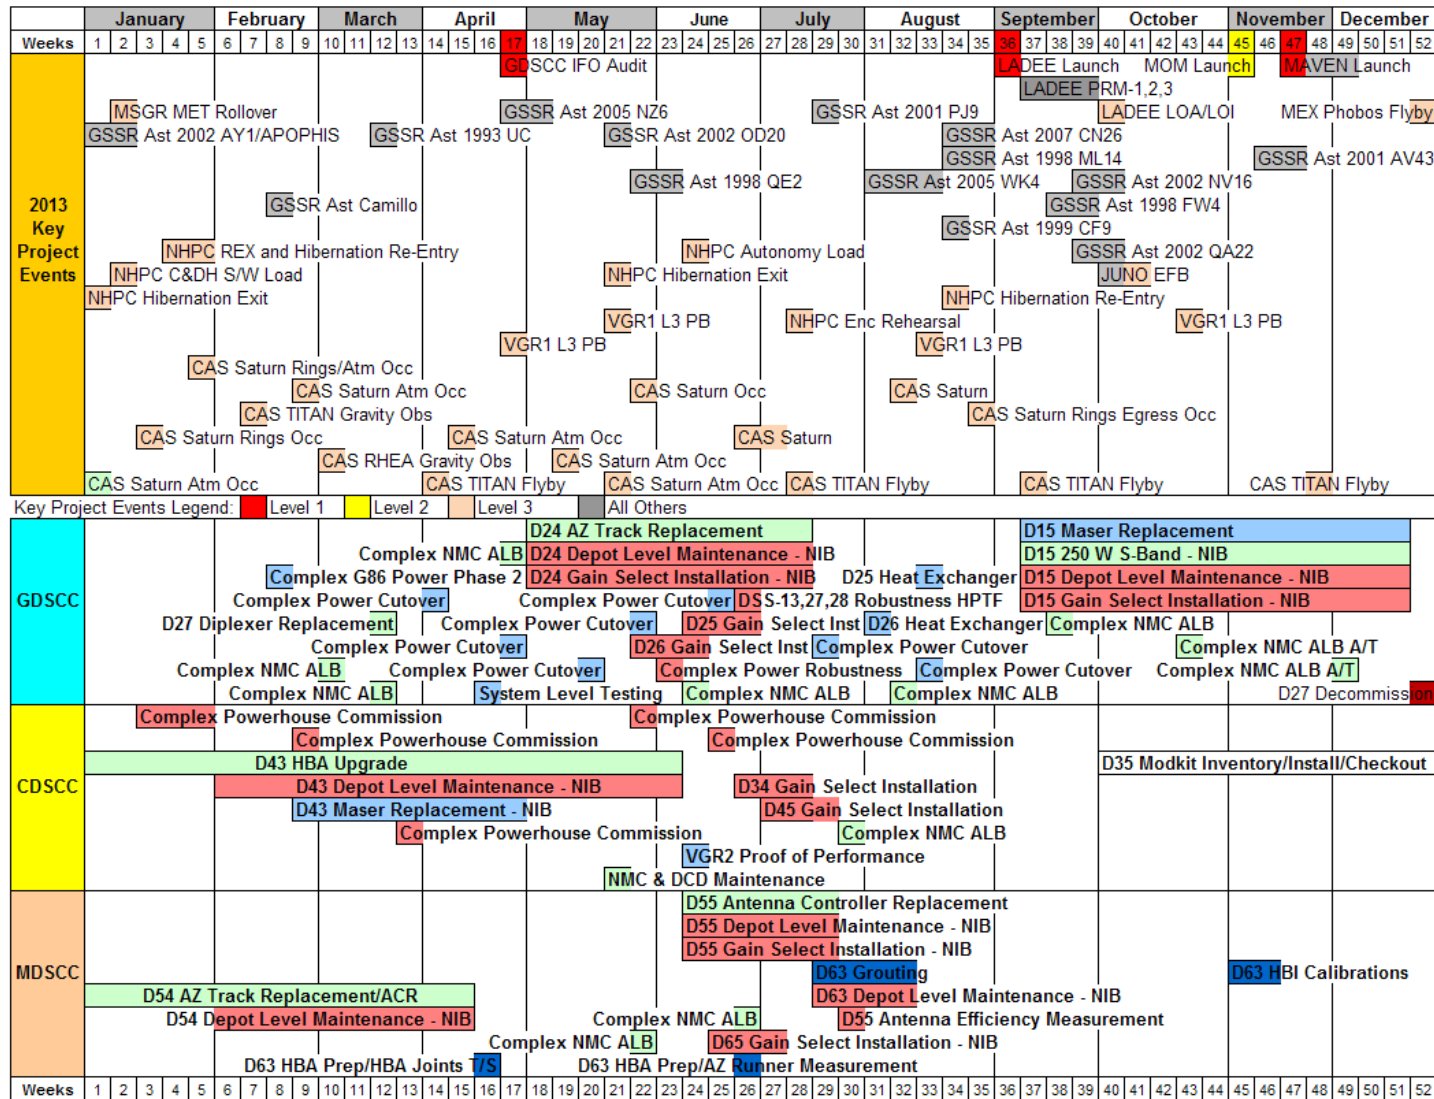

Revised: October 29, 2013




Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



Jet Propulsion Laboratory
California Institute of Technology

- 2014 -

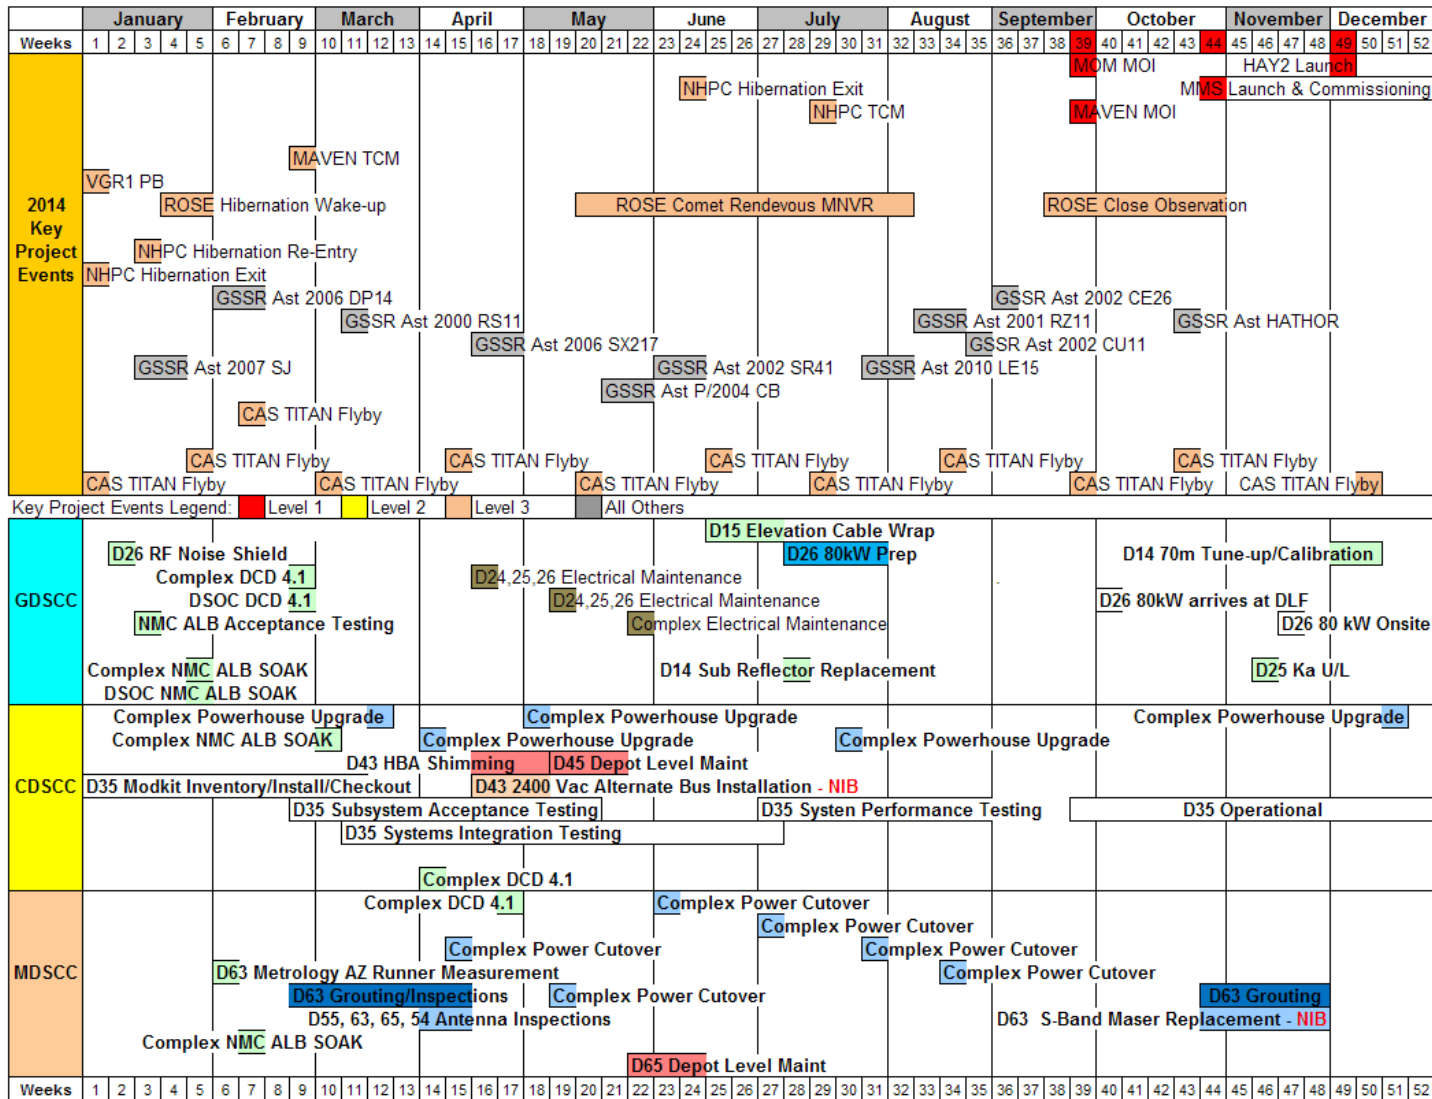


Revised: November 27, 2013




JPL

Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



- 2015 -

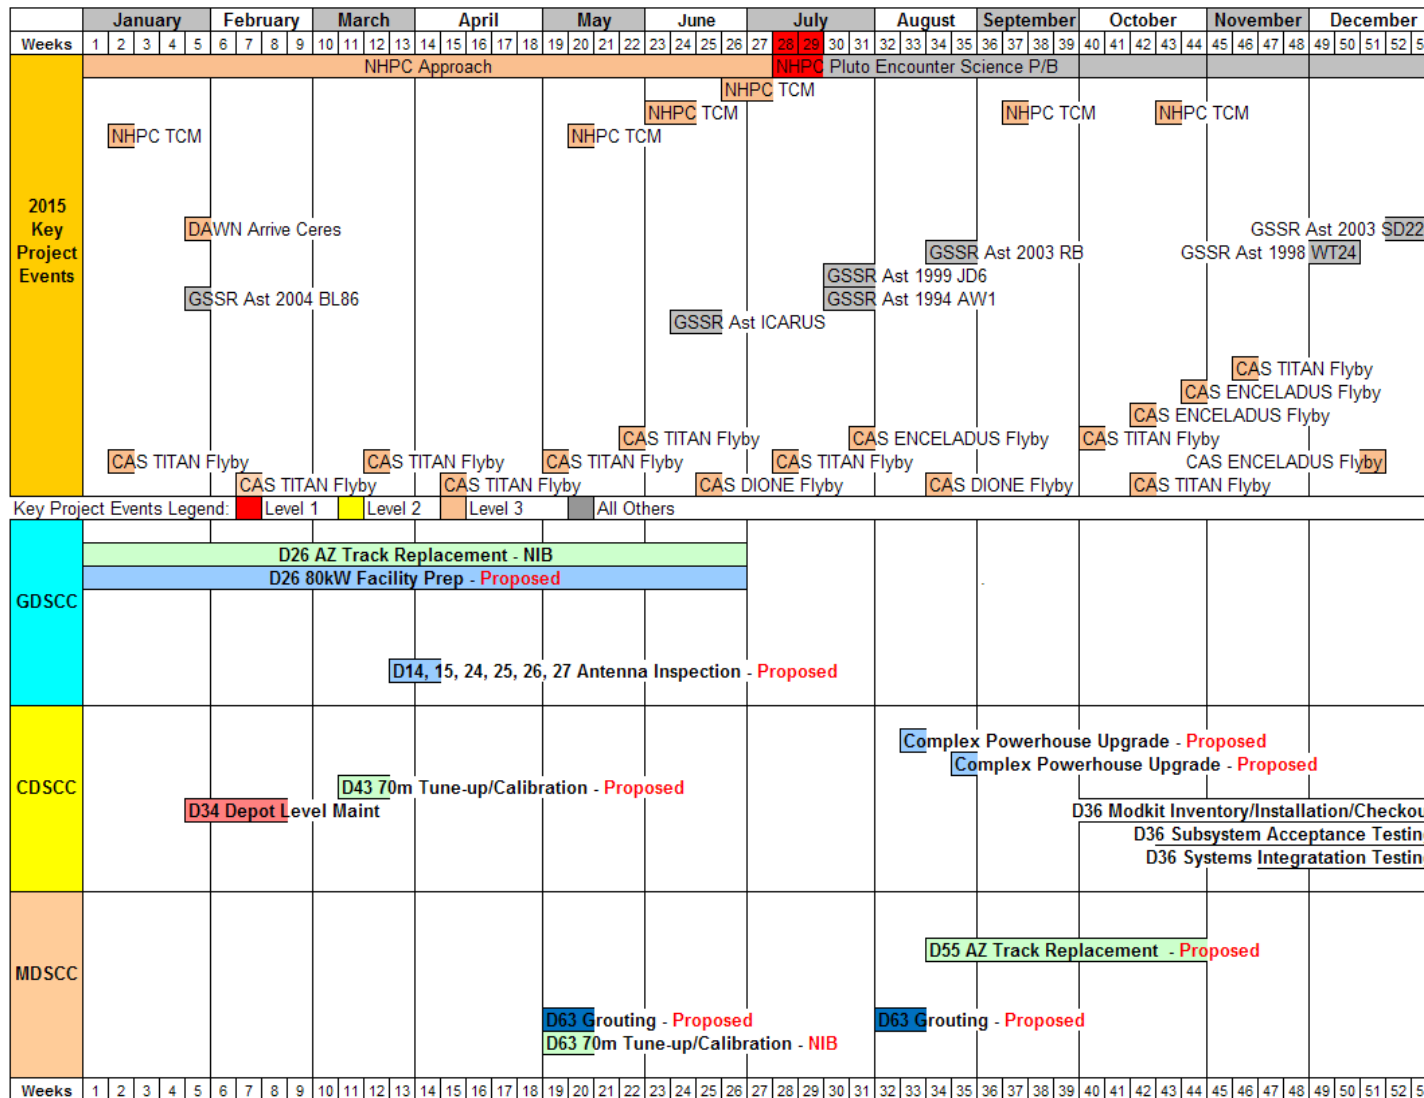


Revised: November 22, 2013



JPL

Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




- 2016 -

	January				February				March				April				May				June				July				August				September				October				November				December								
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	
2016 Key Project Events	ExoMars Launch								InSight Launch												JUNO JOI								InSight EDL																								
																					JUNO GDSCC/CAN Array supports				JUNO GDSCC Array supports																												
																					JUNO JOI Cleanup				JUNO Capture Orbit																												
					CAS TITAN Flyby				CAS TITAN Flyby								CAS TITAN Flyby								CAS TITAN Flyby				CAS TITAN Flyby				CAS TITAN Flyby				CAS TITAN Flyby																
Key Project Events Legend: ■ Level 1 ■ Level 2 ■ Level 3 ■ All Others																																																					
GDSCC																																									D14 APCA - Proposed												
CDSCC	D34,35,43,45 Antenna Inspection - Proposed																												SWUPS Installation - Proposed				SWUPS Installation - Proposed				SWUPS Installation - Proposed																
																																	D36 Operational																				
MDSCC														D63 Grouting - Proposed																	D63 Grouting - Proposed																						
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	

Revised: November 22, 2013



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



Jet Propulsion Laboratory
California Institute of Technology


- 2017 -

	January				February				March				April				May				June				July				August				September				October				November				December							
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52
2017 Key Project Events																																																				
CAS TITAN Flyby																																																				
Key Project Events Legend: ■ Level 1 ■ Level 2 ■ Level 3 ■ All Others																																																				
GDSCC	D14 APCA - Proposed																																																			
CDSCC	D43 APCA - Proposed																																																			
MDSCC	D63 HBA Upgrades & Life Extension - Proposed D63 APCA - NIB D54,55,63, 65 Antenna Inspection - Proposed																																																			
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52

Revised: September 30, 2013



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



Jet Propulsion Laboratory
California Institute of Technology


- 2018 -

	January				February				March				April				May				June				July				August				September				October				November				December											
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52				
2018 Key Project Events															Mars 2018 Launch and LEOP														SP Launch and LEOP														JWST Launch and Commissioning													
Key Project Events Legend: ■ Level 1 ■ Level 2 ■ Level 3 ■ All Others																																																								
GDSCC	D25 XX/Ka Installation - Proposed														D25 AZ Track Replacement - NIB														D24 XX/Ka Installation - Proposed														D24 Ka2 Tune-up NIB													
															D14, 15, 25, 26, 24, 15, 27 Antenna Inspection - Proposed																																									
CDSCC																													D34 Ka2 Tune-up																											
MDSCC																																											D54 Pedestal Rehab - Proposed													
																																											D54 Ka2 Tune-up NIB													
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52				

Revised: October 15, 2013



Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



Jet Propulsion Laboratory
California Institute of Technology

- 2019 -


	January					February					March					April					May					June					July					August					September					October					November					December				
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52								
2019 Key Project Events								SPP Beacon					SPP Solar Enc											ORX Tag 1 Reh													SPP Solar Enc															SPP Venus Flyby								
Key Project Events Legend: ■ Level 1 ■ Level 2 ■ Level 3 ■ All Others																																																												
GDSCC																																																												
CDSCC																																																												
MDSCC																																																												
Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52								

Revised: April 25, 2013



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2013

2013							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 15	250W S-Band - NIB	09/09/2013 15:00	12/21/2013 00:00	102	37 - 51	252	355
DSS 15	Depot Level Maintenance - NIB	09/09/2013 15:00	12/21/2013 00:00	102	37 - 51	252	355
DSS 15	Gain Select Installation - NIB	09/09/2013 15:00	12/21/2013 00:00	102	37 - 51	252	355
DSS 15	Maser Replacement	09/09/2013 15:00	12/21/2013 00:00	102	37 - 51	252	355
SPC 10	NMC Automated Link Build - Acceptance testing	12/03/2013 02:45	12/03/2013 08:45	0	49 - 49	337	337



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2014

2014							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 26	RF Noise Shield	01/09/2014 16:00	01/10/2014 00:00	0	02 - 02	9	10
DSS 26	RF Noise Shield	01/10/2014 16:00	01/11/2014 00:00	0	02 - 02	10	11
SPC 10	NMC Acceptance Testing	01/16/2014 00:00	01/16/2014 06:00	0	03 - 03	16	16
GCF 20	DSOC NMC ALB SOAK	01/31/2014 00:00	01/31/2014 06:00	0	05 - 05	31	31
SPC 10	NMC ALB SOAK	02/02/2014 00:45	02/02/2014 06:45	0	05 - 05	33	33
DSS 63	Metrology AZ Runner Measurement	02/03/2014 19:00	02/04/2014 01:20	0	06 - 06	34	35
DSS 63	Metrology AZ Runner Measurement	02/04/2014 19:00	02/05/2014 07:00	0	06 - 06	35	36
DSS 63	Metrology AZ Runner Measurement	02/05/2014 19:00	02/06/2014 07:00	0	06 - 06	36	37
DSS 63	Metrology AZ Runner Measurement	02/06/2014 19:00	02/07/2014 07:00	0	06 - 06	37	38
SPC 60	NMC ALB SOAK	02/16/2014 06:00	02/16/2014 14:00	0	07 - 07	47	47
DSS 63	Grouting	02/24/2014 06:00	04/11/2014 17:00	46	09 - 15	55	101
SPC 10	DCD 4.1	02/24/2014 20:00	02/25/2014 00:00	0	09 - 09	55	56
GCF 20	DSOC DCD 4.1	02/24/2014 20:00	02/25/2014 00:00	0	09 - 09	55	56
SPC 40	NMC Automated Link Build - SOAK	03/05/2014 21:00	03/06/2014 05:00	0	10 - 10	64	65
SPC 40	Complex Powerhouse Upgrade	03/21/2014 21:00	03/22/2014 09:00	0	12 - 12	80	81
DSS 55	Antenna Inspection	03/31/2014 06:00	03/31/2014 14:00	0	14 - 14	90	90
DSS 65	Antenna Inspection	04/01/2014 06:00	04/01/2014 14:00	0	14 - 14	91	91
DSS 63	Antenna Inspection	04/02/2014 06:00	04/02/2014 14:00	0	14 - 14	92	92
SPC 40	DCD 4.1	04/02/2014 23:00	04/03/2014 05:00	0	14 - 14	92	93
DSS 54	Antenna Inspection	04/04/2014 06:00	04/04/2014 14:00	0	14 - 14	94	94
SPC 40	Complex Powerhouse Upgrade	04/04/2014 21:00	04/05/2014 03:00	0	14 - 14	94	95
DSS 55	Antenna Inspection	04/07/2014 06:00	04/07/2014 18:00	0	15 - 15	97	97
SPC 60	Complex Power Cutover	04/08/2014 05:00	04/08/2014 17:00	0	15 - 15	98	98



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2014

2014							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 65	Antenna Inspection	04/08/2014 06:00	04/08/2014 18:00	0	15 - 15	98	98
DSS 63	Antenna Inspection	04/09/2014 06:00	04/09/2014 18:00	0	15 - 15	99	99
DSS 54	Antenna Inspection	04/11/2014 06:00	04/11/2014 18:00	0	15 - 15	101	101
DSS 43	2400 Vac Alternate Bus Installatation - NIB	04/14/2014 21:00	05/02/2014 05:00	17	16 - 18	104	122
DSS 43	HBA Shimming	04/14/2014 21:00	05/02/2014 05:00	17	16 - 18	104	122
DSS 24	Electrical Maintenance	04/16/2014 15:00	04/17/2014 03:00	0	16 - 16	106	107
DSS 25	Electrical Maintenance	04/16/2014 15:00	04/17/2014 03:00	0	16 - 16	106	107
DSS 26	Electrical Maintenance	04/16/2014 15:00	04/17/2014 03:00	0	16 - 16	106	107
SPC 60	DCD 4.1	04/23/2014 07:00	04/23/2014 13:00	0	17 - 17	113	113
SPC 40	Complex Powerhouse Upgrade	04/30/2014 21:00	05/01/2014 03:00	0	18 - 18	120	121
DSS 45	Depot Level Maintenance	05/05/2014 21:00	05/23/2014 06:00	17	19 - 21	125	143
DSS 24	Electrical Maintenance	05/06/2014 14:00	05/07/2014 02:00	0	19 - 19	126	127
DSS 25	Electrical Maintenance	05/06/2014 14:00	05/07/2014 02:00	0	19 - 19	126	127
DSS 26	Electrical Maintenance	05/06/2014 14:00	05/07/2014 02:00	0	19 - 19	126	127
SPC 60	Complex Power Cutover	05/09/2014 05:00	05/09/2014 17:00	0	19 - 19	129	129
DSS 65	Depot Level Maintenance	05/26/2014 06:00	06/13/2014 17:00	18	22 - 24	146	164
SPC 10	Complex Electrical Maintenance	05/27/2014 13:00	05/28/2014 01:00	0	22 - 22	147	148
DSS 26	80KW Prep	06/02/2014 14:00	06/27/2014 02:00	24	23 - 26	153	178
SPC 60	Complex Power Cutover	06/04/2014 05:00	06/04/2014 17:00	0	23 - 23	155	155
DSS 15	Elevation Cable Wrap	06/16/2014 15:00	07/04/2014 00:00	17	25 - 27	167	185
SPC 60	Complex Power Cutover	07/03/2014 05:00	07/03/2014 17:00	0	27 - 27	184	184
DSS 26	80KW Prep	07/07/2014 14:00	08/02/2014 00:00	25	28 - 31	188	214
DSS 14	Sub Reflector Replacement	07/07/2014 16:00	07/10/2014 00:00	2	28 - 28	188	191



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2014

2014							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 14	Sub Reflector Replacement	07/10/2014 16:00	07/11/2014 00:00	0	28 - 28	191	192
DSS 14	Sub Reflector Replacement	07/11/2014 16:00	07/12/2014 00:00	0	28 - 28	192	193
DSS 15	Elevation Cable Wrap	07/14/2014 15:00	08/01/2014 00:00	17	29 - 31	195	213
SPC 40	Complex Powerhouse Upgrade	07/23/2014 21:00	07/24/2014 03:00	0	30 - 30	204	205
SPC 60	Complex Power Cutover	07/30/2014 05:00	07/30/2014 17:00	0	31 - 31	211	211
SPC 60	Complex Power Cutover	08/20/2014 05:00	08/20/2014 17:00	0	34 - 34	232	232
DSS 63	Grouting	10/27/2014 06:00	11/28/2014 17:00	32	44 - 48	300	332
DSS 63	S-Band Maser Replacement - NIB	11/03/2014 06:00	11/28/2014 17:00	25	45 - 48	307	332
DSS 25	Ka uplink	11/10/2014 14:00	11/17/2014 00:00	6	46 - 47	314	321
DSS 14	70M Tune-up/Calibration	12/01/2014 15:00	12/15/2014 00:00	13	49 - 51	335	349
SPC 40	Complex Powerhouse Upgrade	12/16/2014 21:00	12/17/2014 03:00	0	51 - 51	350	351
SPC 40	Complex Powerhouse Upgrade	12/17/2014 21:00	12/18/2014 03:00	0	51 - 51	351	352
DSS 26	80kW Prep - Proposed	12/29/2014 15:00	06/27/2015 00:00	179	01 - 26	363	178
DSS 26	AZ Track Replacement - NIB	12/29/2014 15:00	06/27/2015 00:00	179	01 - 26	363	178



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2015

2015							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 34	Depot Level Maintenance	01/26/2015 21:00	02/20/2015 05:00	24	05 - 08	26	51
DSS 43	70m Tune-up/Calibration - Proposed	03/09/2015 21:00	03/21/2015 06:00	11	11 - 12	68	80
SPC 40	Complex Powerhouse Upgrade - Proposed	03/19/2015 21:00	03/20/2015 03:00	0	12 - 12	78	79
DSS 14	Antenna Inspection - Proposed	03/23/2015 15:00	03/24/2015 03:00	0	13 - 13	82	83
DSS 26	Antenna Inspection - Proposed	03/24/2015 15:00	03/25/2015 03:00	0	13 - 13	83	84
DSS 24	Antenna Inspection - Proposed	03/25/2015 15:00	03/26/2015 03:00	0	13 - 13	84	85
DSS 25	Antenna Inspection - Proposed	03/25/2015 15:00	03/26/2015 03:00	0	13 - 13	84	85
DSS 15	Antenna Inspection - Proposed	03/26/2015 15:00	03/27/2015 03:00	0	13 - 13	85	86
DSS 14	Antenna Inspection - Proposed	03/27/2015 15:00	03/28/2015 03:00	0	13 - 13	86	87
DSS 27	Antenna Inspection - Proposed	03/27/2015 15:00	03/28/2015 03:00	0	13 - 13	86	87
DSS 26	Antenna Inspection - Proposed	03/31/2015 15:00	04/01/2015 03:00	0	14 - 14	90	91
DSS 25	Antenna Inspection - Proposed	04/01/2015 15:00	04/02/2015 03:00	0	14 - 14	91	92
DSS 24	Antenna Inspection - Proposed	04/01/2015 15:00	04/02/2015 03:00	0	14 - 14	91	92
DSS 15	Antenna Inspection - Proposed	04/02/2015 15:00	04/03/2015 03:00	0	14 - 14	92	93
DSS 27	Antenna Inspection - Proposed	04/03/2015 15:00	04/04/2015 03:00	0	14 - 14	93	94
DSS 63	70m Tune-up/Calibration - NIB	05/04/2015 06:00	05/17/2015 17:00	13	19 - 20	124	137
DSS 63	Grouting - Proposed	05/04/2015 06:00	05/17/2015 17:00	13	19 - 20	124	137
DSS 63	Grouting - Proposed	08/03/2015 05:00	08/16/2015 17:00	14	32 - 33	215	228
SPC 40	Complex Powerhouse Upgrade - Proposed	08/12/2015 21:00	08/13/2015 09:00	0	33 - 33	224	225
DSS 55	AZ Track Replacement - Proposed	08/17/2015 06:00	10/31/2015 00:00	75	34 - 44	229	304
SPC 40	Complex Powerhouse Upgrade	08/26/2015 21:00	08/27/2015 03:00	0	35 - 35	238	239



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2016

2016							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 43	Antenna Inspection - Proposed	01/04/2016 22:00	01/05/2016 14:00	1	01 - 01	4	5
DSS 34	Antenna Inspection - Proposed	01/05/2016 22:00	01/06/2016 14:00	1	01 - 01	5	6
DSS 45	Antenna Inspection - Proposed	01/06/2016 22:00	01/07/2016 14:00	1	01 - 01	6	7
DSS 35	Antenna Inspection - Proposed	01/07/2016 22:00	01/08/2016 14:00	1	01 - 01	7	8
DSS 43	Antenna Inspection - Proposed	01/11/2016 22:00	01/12/2016 06:00	0	02 - 02	11	12
DSS 34	Antenna Inspection - Proposed	01/12/2016 22:00	01/13/2016 06:00	0	02 - 02	12	13
DSS 63	Grouting - Proposed	04/04/2016 06:00	04/29/2016 17:00	25	14 - 17	95	120
DSS 63	Grouting - Proposed	10/03/2016 06:00	10/28/2016 17:00	25	40 - 43	277	302
DSS 14	APCA - Proposed	10/31/2016 15:00	01/27/2017 00:00	87	44 - 04	305	27
SPC 40	SWUPS Installation - Proposed	11/02/2016 21:00	11/03/2016 09:00	0	44 - 44	307	308
SPC 40	SWUPS Installation - Proposed	11/16/2016 21:00	11/17/2016 09:00	0	46 - 46	321	322
SPC 40	SWUPS Installation - Proposed	11/30/2016 21:00	12/01/2016 09:00	0	48 - 48	335	336



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2017

2017							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 63	APCA - NIB	01/30/2017 06:00	09/08/2017 17:00	221	05 - 36	30	251
DSS 63	HBA Upgrade and Life Extension - Proposed	01/30/2017 06:00	09/08/2017 17:00	221	05 - 36	30	251
DSS 55	Antenna Inspection - Proposed	08/28/2017 07:00	08/28/2017 23:00	1	35 - 35	240	240
DSS 65	Antenna Inspection - Proposed	08/29/2017 07:00	08/29/2017 23:00	1	35 - 35	241	241
DSS 63	Antenna Inspection - Proposed	08/30/2017 07:00	08/30/2017 23:00	1	35 - 35	242	242
DSS 54	Antenna Inspection - Proposed	08/31/2017 07:00	08/31/2017 23:00	1	35 - 35	243	243
DSS 55	Antenna Inspection - Proposed	09/04/2017 07:00	09/04/2017 15:00	0	36 - 36	247	247
DSS 63	Antenna Inspection - Proposed	09/05/2017 07:00	09/05/2017 15:00	0	36 - 36	248	248
DSS 54	Antenna Inspection - Proposed	09/07/2017 07:00	09/07/2017 15:00	0	36 - 36	250	250
DSS 43	APCA - Proposed	09/11/2017 21:00	12/01/2017 06:00	80	37 - 48	254	335



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service




DSN Downtime 2018

2018							
Site	Details	Start	End	Duration (Days)	Weeks	Start DOY	End DOY
DSS 25	XX/Ka Installation - Proposed	01/04/2018 15:00	04/07/2018 00:00	92	01 - 14	4	97
DSS 54	Pedestal Rehab	01/08/2018 06:00	09/28/2018 17:00	263	02 - 39	8	271
DSS 25	AZ Track Replacement - NIB	01/29/2018 15:00	04/07/2018 00:00	67	05 - 14	29	97
DSS 14	Antenna Inspection - Proposed	04/08/2018 15:00	04/09/2018 06:00	1	14 - 15	98	99
DSS 26	Antenna Inspection - Proposed	04/09/2018 15:00	04/10/2018 06:00	1	15 - 15	99	100
DSS 25	Antenna Inspection - Proposed	04/10/2018 15:00	04/11/2018 06:00	1	15 - 15	100	101
DSS 15	Antenna Inspection - Proposed	04/11/2018 15:00	04/12/2018 06:00	1	15 - 15	101	102
DSS 27	Antenna Inspection - Proposed	04/12/2018 15:00	04/13/2018 06:00	1	15 - 15	102	103
DSS 14	Antenna Inspection - Proposed	04/15/2018 15:00	04/16/2018 00:00	0	15 - 16	105	106
DSS 26	Antenna Inspection - Proposed	04/16/2018 15:00	04/17/2018 00:00	0	16 - 16	106	107
DSS 24	Antenna Inspection - Proposed	04/17/2018 15:00	04/18/2018 06:00	1	16 - 16	107	108
DSS 27	Antenna Inspection - Proposed	04/18/2018 15:00	04/19/2018 00:00	0	16 - 16	108	109
DSS 24	Ka2 Tune-up - NIB	04/30/2018 15:00	05/13/2018 00:00	12	18 - 19	120	133
DSS 24	XX/Ka Installation - Proposed	04/30/2018 15:00	07/07/2018 00:00	67	18 - 27	120	188
DSS 34	Ka2 Tune-up - Proposed	05/28/2018 21:00	06/04/2018 06:00	6	22 - 23	148	155
DSS 54	Ka2 Tune-up - NIB	09/03/2018 06:00	09/17/2018 17:00	14	36 - 38	246	260



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



Future assets new/upgrades

- DSS-35 Installation and Operational 2013 – 2014
 - Modkit Installation October 1, 2013 – March 14, 2014 weeks 40 – 11
 - Acceptance Testing February 25, 2014 – May 12, 2013, weeks 09 – 20
 - System Integration Testing March 14, 2014 – June 30, 2014 weeks 11 – 27
 - Operations Systems Performance Testing June 30, 2014 – August 28, 2014, weeks 27 – 35
 - Operational September 26, 2014


- DSS-26 80kW Installation 2014 – 2015
 - 80kW arrive at DLF October, 2014, week 40
 - DDR September, 2015, week 38

- DSS-36 Installation and Operational 2016 – A placeholder has been set awaiting dates



Jet Propulsion Laboratory
California Institute of Technology

Interplanetary Network Directorate (IND) Deep Space Network (DSN) Resource Allocation Planning Service



Antenna Downtime Status and Forecast

DSN Resource Implementation Planning Matrix by Complex

Complex	Station	Subnet	S-Band		X-Band		Ka-Band		Ka Phase 2	X-Band ACQ AID	80KW
			Down	Up	Down	Up	Down	Up			
10	DSS-27	34HSB #	✓	✓	N/A	N/A	N/A	N/A	N/A	N/A	N/A
10	DSS-24	34B1	✓	✓	✓	✓	N/A	N/A	✓	✓	N/A
10	DSS-25	34B2	N/A	N/A	✓	✓	✓	✓	N/A	N/A	N/A
10	DSS-26	34B2	N/A	N/A	✓	✓	✓	N/A	N/A	N/A	10/01/15
10	DSS-15	34HEF	✓	12/21/13	✓	✓	N/A	N/A	N/A	N/A	N/A
10	DSS-14	70M	✓	✓	✓	✓	N/A	N/A	N/A	N/A	N/A
40	DSS-33*	34B2	N/A	N/A	10/01/19	10/01/19	10/01/19	N/A	N/A	N/A	N/A
40	DSS-34	34B1	✓	✓	✓	✓	✓	N/A	✓	✓	N/A
40	DSS-35*	34B2	N/A	N/A	09/29/14	09/29/14	09/29/14	N/A	N/A	N/A	N/A
40	DSS-36*	34B2	N/A	N/A	09/26/16	09/26/16	09/26/16	N/A	N/A	N/A	N/A
40	DSS-45	34HEF	✓	✓	✓	✓	N/A	N/A	N/A	N/A	N/A
40	DSS-43	70M	✓	✓	✓	✓	N/A	N/A	N/A	N/A	N/A
60	DSS-54	34B1	✓	✓	✓	✓	✓	N/A	✓	✓	N/A
60	DSS-55	34B2	N/A	N/A	✓	✓	✓	N/A	N/A	N/A	N/A
60	DSS-56	34B2	N/A	N/A	09/28/20	09/28/20	09/28/20	N/A	N/A	N/A	N/A
60	DSS-65	34HEF	✓	✓	✓	✓	N/A	N/A	N/A	N/A	N/A
60	DSS-63	70M	✓	✓	✓	✓	N/A	N/A	N/A	N/A	N/A

N/A = Not Applicable or Capability Not Planned

xx/xx/xx = Capability Date Recently Changed

As of: 9/16/2013

✓ ✓ ✓ = Capability Recently Exists

✓ = Capability Exists

* = To Be Commissioned

= To Be De-Commissioned - 12/8/2013
